


The Queue - Planned vs. Actual Gantt Chart

Final Project Checkpoint | Daysha Roberts | COSC 4308 | Repository: <https://github.com/xTop5ive/The-Queue>

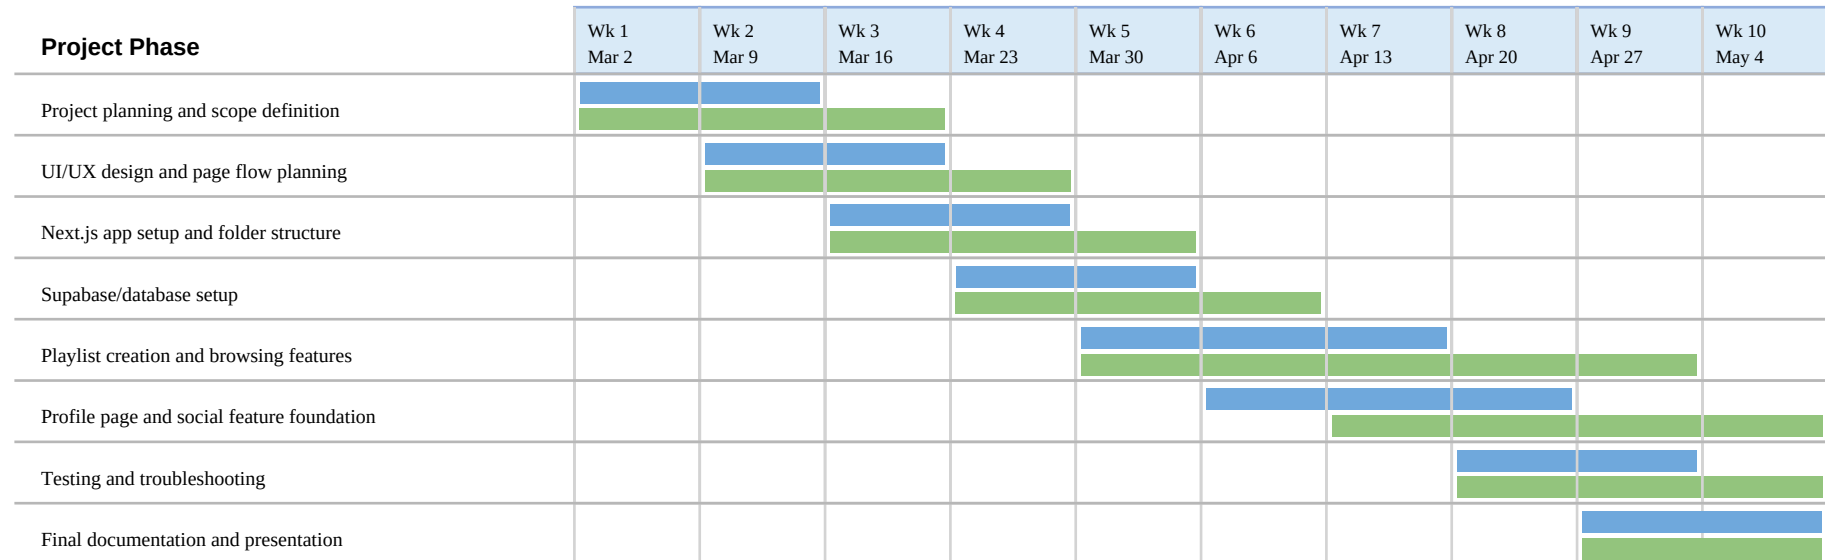

Planned schedule Actual progress

Note: Actual progress extended later for playlist features, profiles, testing, and final documentation due to scope refinement.

Phase	Planned Timeline	Actual Timeline	Status / Notes
Planning and Scope	Mar 2 - Mar 13	Mar 2 - Mar 20	Completed. Scope was refined into a playlist-sharing social music app.
Design	Mar 9 - Mar 20	Mar 9 - Mar 27	Completed with revisions as the app direction became clearer.
Development Setup	Mar 16 - Mar 27	Mar 16 - Apr 10	Completed. Next.js structure and backend setup took longer than planned.
Core Playlist Features	Mar 30 - Apr 17	Mar 30 - Apr 24	Partially completed. Playlist creation, browsing, tags, cover art, and interactions were prioritized.
Profile and Social Features	Apr 6 - Apr 24	Apr 13 - May 4	In progress. Profile and community concepts were started but not fully finished.
Testing and Troubleshooting	Apr 20 - Apr 27	Apr 20 - May 4	Partially completed through development testing and fixes.
Documentation and Final Presentation	Apr 27 - May 5	Apr 27 - May 5	Completed for final checkpoint submission.
